



# FAIRGROUNDS & PENNICHUCK MIDDLE SCHOOL ADDITIONS & RENOVATIONS

NASHUA, NEW HAMPSHIRE

JUNE 2021 PROJECT UPDATES  
HARVEY CONSTRUCTION





# PENNICHUCK MIDDLE SCHOOL CONSTRUCTION PROGRESS



SOUTH, CHORUS & BOILER  
ROOM ADDITIONS IN  
PROGRESS



CONSTRUCTION COMPELTE  
- NORTHEAST PARKING LOT  
(MAY 2021)


- COMPLETED NEW NORTHEAST PARKING AREA
  - BASE PAVE, CURBING, TEMP. STRIPING
- LAST DAY OF SCHOOL = 6/15/2021
- ESTABLISHED SUMMER CONSTRUCTION AREA FENCING - 6/21/2021
- STRIP EXISTING ASPHALT AND TOPSOIL
- ESTABLISH SUBGRADE AND INSTALL UTILITIES
- PREP FOR PAVING, SIDEWALKS & ISLANDS
- FOUNDATIONS FOR NEW SOUTH/NORTH, CHORUS & BOILER ROOM ADDITIONS (SUMMER 2021)





# PMS SUMMER 2021 SITE LOGISTICS

- ACTIVE CONSTRUCTION SITE FOR SUMMER 2021
- CLOSED TO PUBLIC UNTIL START OF SCHOOL YEAR – FALL 2021
- ACCESS TO TRACK PROVIDED FROM HENRI BURQUE HIGHWAY FOOT BRIDGE

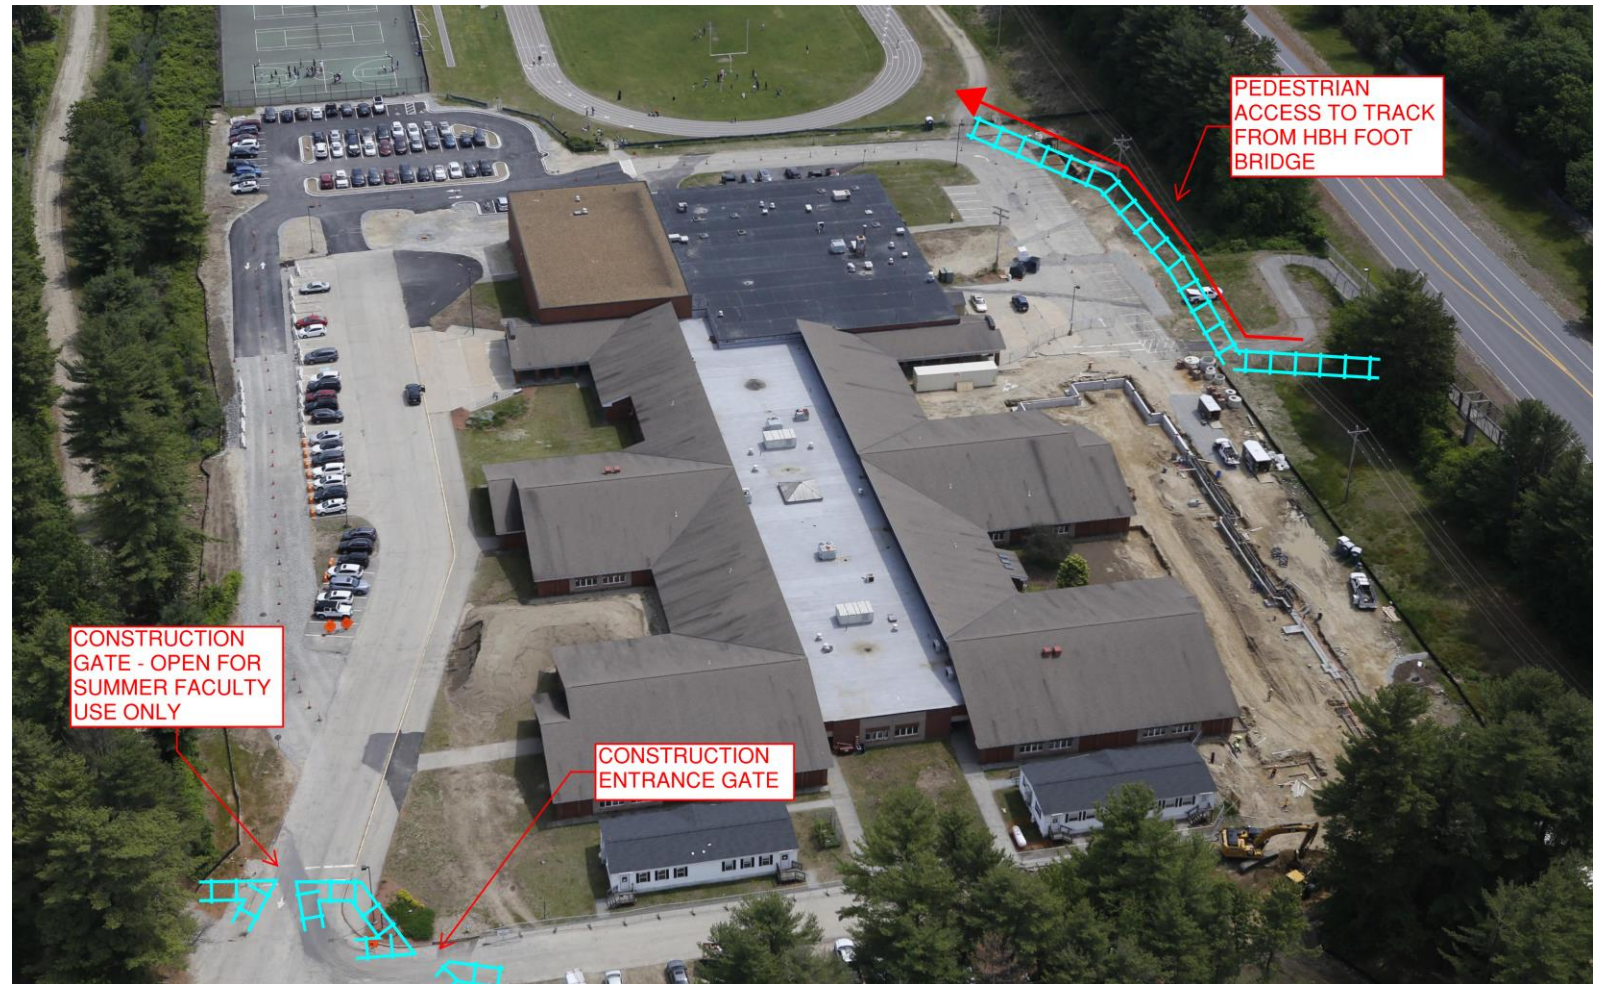





# PMS NORTHEAST PARKING LOT CONSTRUCTION





# PMS SOUTH ADDITION CONSTRUCTION PROGRESS





# PMS SOUTH ADDITION CONSTRUCTION PROGRESS



# FAIRGROUNDS MIDDLE SCHOOL CONSTRUCTION MILESTONES:

- ADDRESSING HARRIMAN/HCC PUNCHLIST ITEMS WITH TRADE CONTRACTORS IN THE FIELD – SUMMER 2021
- INTERIOR – SUMMER 2021:
  - REMAINING SCIENCE ROOMS
  - GYMNASIUM
- EXTERIOR – SUMMER 2021:
  - FINISH PAVING & RE-STRIPING
  - SITE FURNISHINGS & LANDSCAPING
  - CONSTRUCTION CLEANUP & DEMOBILIZATION (JULY/AUGUST)








# FMS NEW FRONT ENTRANCE CONSTRUCTION PROGRESS

- METAL PANEL INSTALLATION COMPLETE
- SUMMER 2021 -
  - COLUMN COVER
  - COURTYARD LANDSCAPING
  - CUSTOM STONE BENCHES





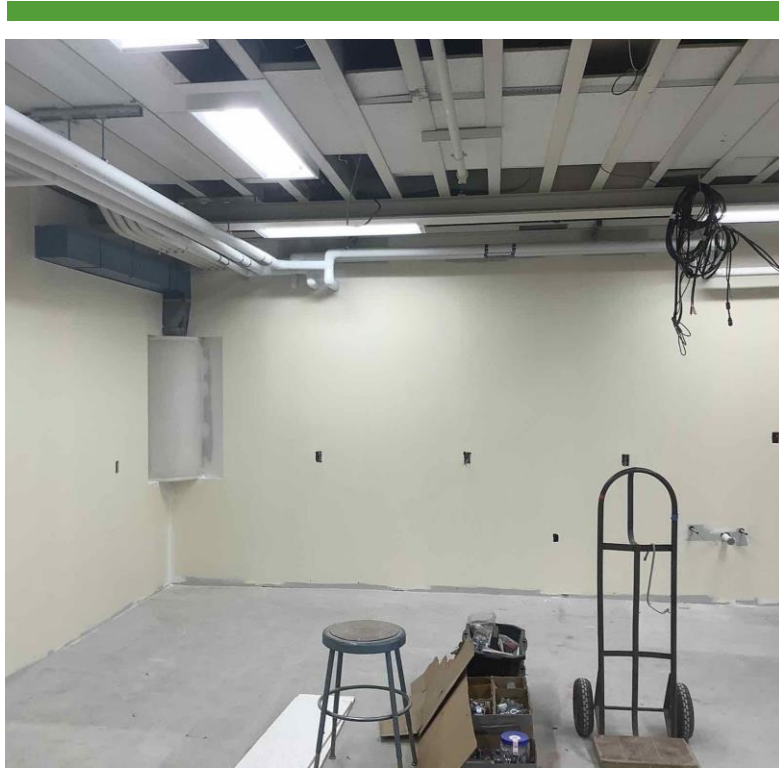


## FMS SCIENCE CLASSROOMS RENOVATION PROGRESS




# FMS GYMNASIUM RENOVATION PROGRESS

- PAINTING OF WALLS & CEILING COMPLETE
- SUMMER 2021 -
  - INSTALL OVERHEAD GYM EQUIPMENT
  - INSTALL NEW WOOD ATHLETIC FLOORING
  - INSTALL NEW BLEACHERS & DIVIDER CURTAIN

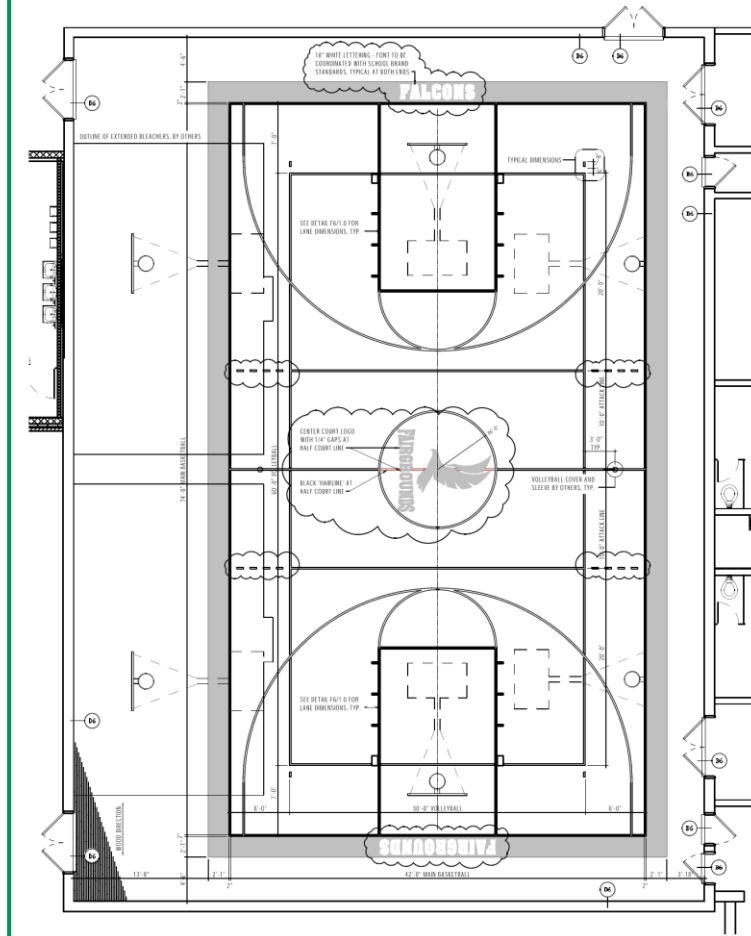



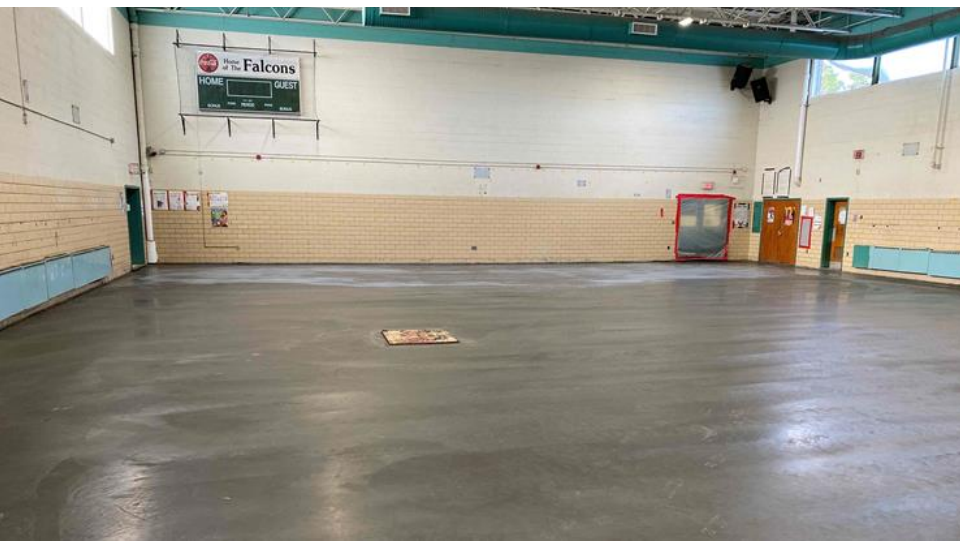

# FMS GYMNASIUM RENOVATION PROGRESS





**HARVEY**
