


Presentation to JSSBC for:

Nashua Middle Schools Projects

Nashua, New Hampshire

November 19, 2020



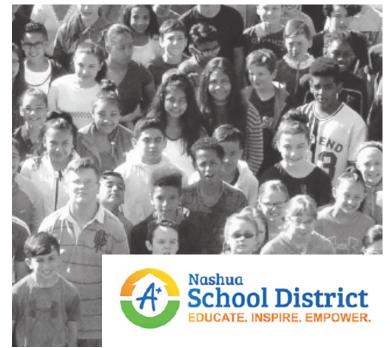

Agenda

- 1. Construction Administration Update
 - a. Fairgrounds Middle School
- 2. Design Milestones and Updates
 - a. Pennichuck Middle School
 - b. New Middle School
- 3. Project Schedule

CONSTRUCTION ADMINISTRATION UPDATE FAIRGROUNDS MIDDLE SCHOOL

Submittals:

Over 140 Submittals received and reviewed

RFI's (Request for Information):

Over 40 received and responded

Proposals (recommended):

- PCO-011 Mop Sink \$0 project add (\$8,794 from contingency)
- PCO-012 Fire Alarm Control Panel \$51,086.90
 - Proposed panel constraints for smoke detection
 - 2 options reviewed

Design Items:

- Corridor Clearances
- Gym Doors
- Building Signage



C.A. UPDATE

"Building a diverse learning community by encouraging students to open their eyes to explore, their minds to create, and their hearts to accept."

FAIRGROUNDS MIDDLE SCHOOL

DESIGN UPDATESPENNICHUCK MIDDLE SCHOOL

Completed Milestones since last JSSBC:

- Planning Board Meeting Site Plan Approval
- Traffic Engineer Meetings
- Meeting with Principal / VP

Upcoming Project Milestones:

Construction Documents Submission


PROJECT PROGRESS

Planning Board:

★ Que Lane

★ Direction Arrows-

★ Dumpster

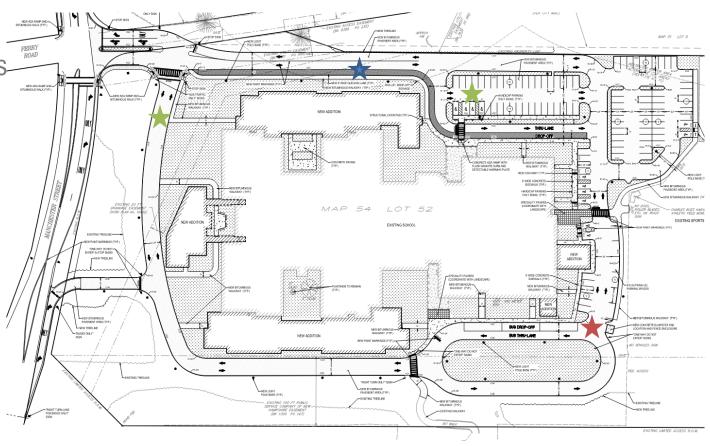


PROJECT PROGRESS |

"Building a diverse learning community by encouraging students to open their eyes to explore, their minds to create, and their hearts to accept."

PENNICHUCK PROGRESS and MILESTONES

Planning Board:

- Traffic Engineer
- ★ Signals
- ★ Turn lane

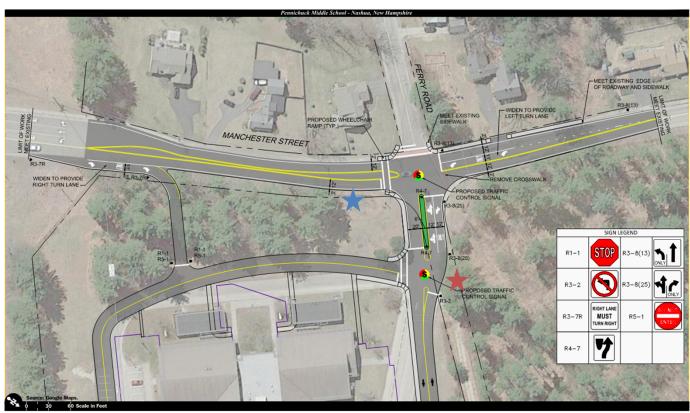

Vanasse & Associates inc
Transportation Engineers & Planners
35 New England Business Center Drive - Suite NA - Andown, MA 01810
www.rdva.com
978-474-8800
1978-474-8800

Pennichuck Middle School Conceptual Improvement Plan

PROJECT PROGRESS |

"Building a diverse learning community by encouraging students to open their eyes to explore, their minds to create, and their hearts to accept."

PENNICHUCK PROGRESS and MILESTONES

DESIGN UPDATESNEW MIDDLE SCHOOL

Completed Milestones since last JSSBC:

• Design Development Submission – October 30, 2020

Upcoming Project Milestones:

Planning Board Submission

PROJECT PROGRESS |

SCHEDULE

