An aerial photograph of a school building complex. The main building is highlighted in a light blue color, indicating areas under renovation or addition. A central courtyard area is highlighted in green. The surrounding area includes parking lots, roads, and other buildings. The text is overlaid on the top left of the image.

FAIRGROUNDS & PENNICHUCK MIDDLE SCHOOL ADDITIONS & RENOVATIONS

NASHUA, NEW HAMPSHIRE

SEPTEMBER 2020 PROJECT UPDATE

HARVEY CONSTRUCTION




PENNICHUCK MIDDLE SCHOOL CONSTRUCTION PROGRESS MILESTONES

INTERIOR RENOVATION OF MAIN ENTRY VESTIBULE
& SECURITY WINDOW SUBSTANTIALLY COMPLETED SEPTEMBER 2020
** NEW CABINET UNIT HEATER & BULLETPROOF TRANSACTION WINDOW TO BE
INSTALLED ONCE MATERIAL/EQUIPMENT ARRIVES ON SITE.*



EXTERIOR SITEWORK, UTILITIES ON-GOING IN
PREPARATION FOR SPRING 2021 RENOVATION/ADDITIONS
(SCHEDULED COMPLETION OCTOBER 2020)

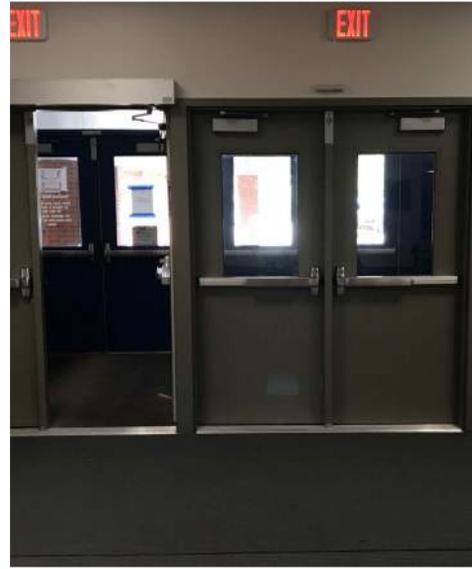

PENNICHUCK MIDDLE SCHOOL CONSTRUCTION PROGRESS PHOTOS

FAIRGROUNDS MIDDLE SCHOOL CONSTRUCTION PROGRESS MILESTONES


EXTERIOR SITEWORK, UTILITIES
& PORTABLE CLASSROOMS (SUMMER 2020)



SCOPE OF WORK FOR PHASES 1, 2, 3 & 4
IN PROGRESS (SUMMER & FALL 2020/WINTER 2021)



PHASE 1 (NEW ENTRY/ADMIN. AREA) = FEBRUARY 2021 TURNOVER
PHASES 2, 3 & 4 = JANUARY 2021 TURNOVER (STUDENTS RETURN)



SITWORK & EXTERIOR IMPROVEMENTS

- SECURITY FENCING INSTALLED AT PERIMETER OF CONSTRUCTION AREAS
- UTILITY WORK ON-GOING
- NEW FIRE LANE COMPLETE
- GRAVEL PREP FOR NEW PARKING AREAS COMPLETE
- ALL SITWORK AND PAVING TO BE COMPLETED FALL 2020.
 - REMAINING EXTERIOR IMPROVEMENTS (BENCHES, FENCING ETC.) TO BE COMPLETED SPRING 2021



FIRE LANE/ACCESS ROAD AT EXTERIOR OF 8TH GRADE WING



ACCESS WALKWAY PREPPED FOR ASPHALT PLACEMENT



NEW RETAINING WALL




NEW PARKING AREA BEING PREPPED FOR PAVING AT THE GYM EXTERIOR/ADJACENT TO TRACK

SITWORK PROGRESS PHOTOS

PORTABLE CLASSROOMS

- 2 PORTABLE CLASSROOM STRUCTURES (4 TOTAL CLASSROOMS)
- REMAINING WORK:
 - FINAL RAMPS
 - SKIRTING AROUND THE BOTTOM PERIMETER OF THE CLASSROOMS
 - JERSEY BARRIERS/FENCING FOR STUDENT/AUTOMOBILE PROTECTION
- TURNOVER DATE = OCTOBER 2020
 - READY FOR TEACHER OCCUPANCY OCTOBER 5, 2020

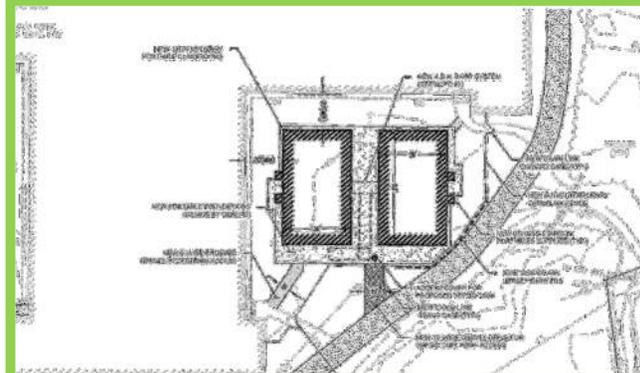



ADMINISTRATION AREA DEMOLITION PROGRESS AT INTERIOR AND EXTERIOR.



PHASE #1 PROGRESS PHOTOS




PHASE 2 PROGRESS PHOTOS




PHASE 2 PROGRESS PHOTOS

PHASE #3 CONSTRUCTION

- RENOVATION OF THE 6TH, 7TH, & 8TH GRADE STUDENT COMMONS AND ADJACENT CORRIDOR AREAS
- REMOVED EXISTING LOCKERS, CASEWORK AND EXISTING FLOORING
- METAL FRAMING COMPLETE
- FLOORING/PAINTING IN PROGRESS
- TURNOVER DATE = OCTOBER 2020
 - AREAS WILL BE READY FOR OCCUPANCY (FINISHES COMPLETE)
 - REMAINING LONG-LEAD ITEMS (MISC. LIGHTING, LOCKERS, MILLWORK, MISC. MECHANICAL EQUIPMENT) WILL BE INSTALLED WHILE THE SPACES ARE UNOCCUPIED
 - HARVEY CONSTRUCTION WILL COORDINATE ALL WORK WITH THE SCHOOL ADMINISTRATION AND STAFF ACCORDINGLY

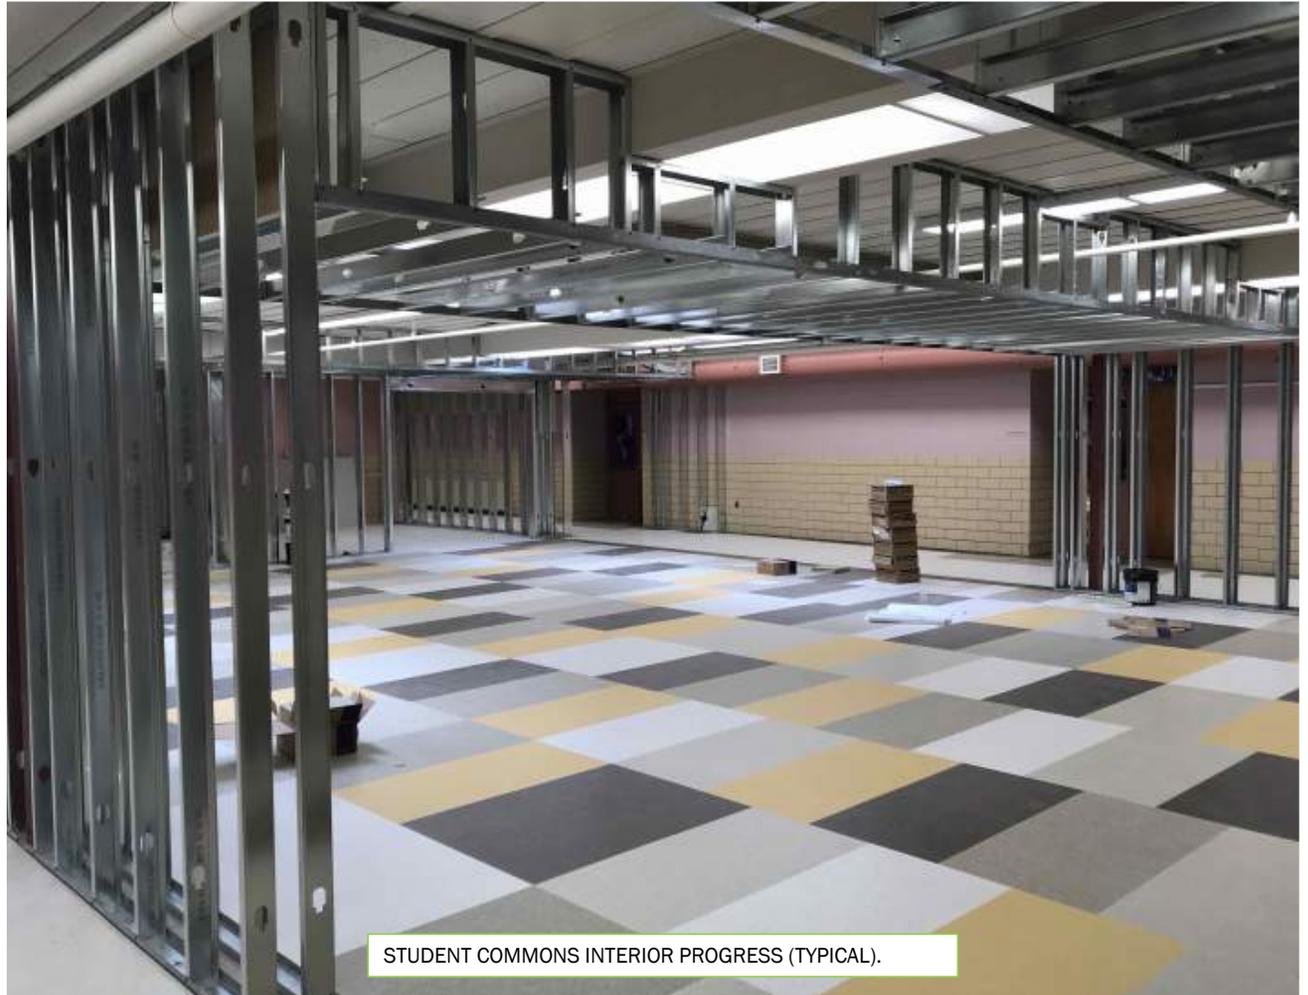

STUDENT COMMONS INTERIOR PROGRESS (TYPICAL).

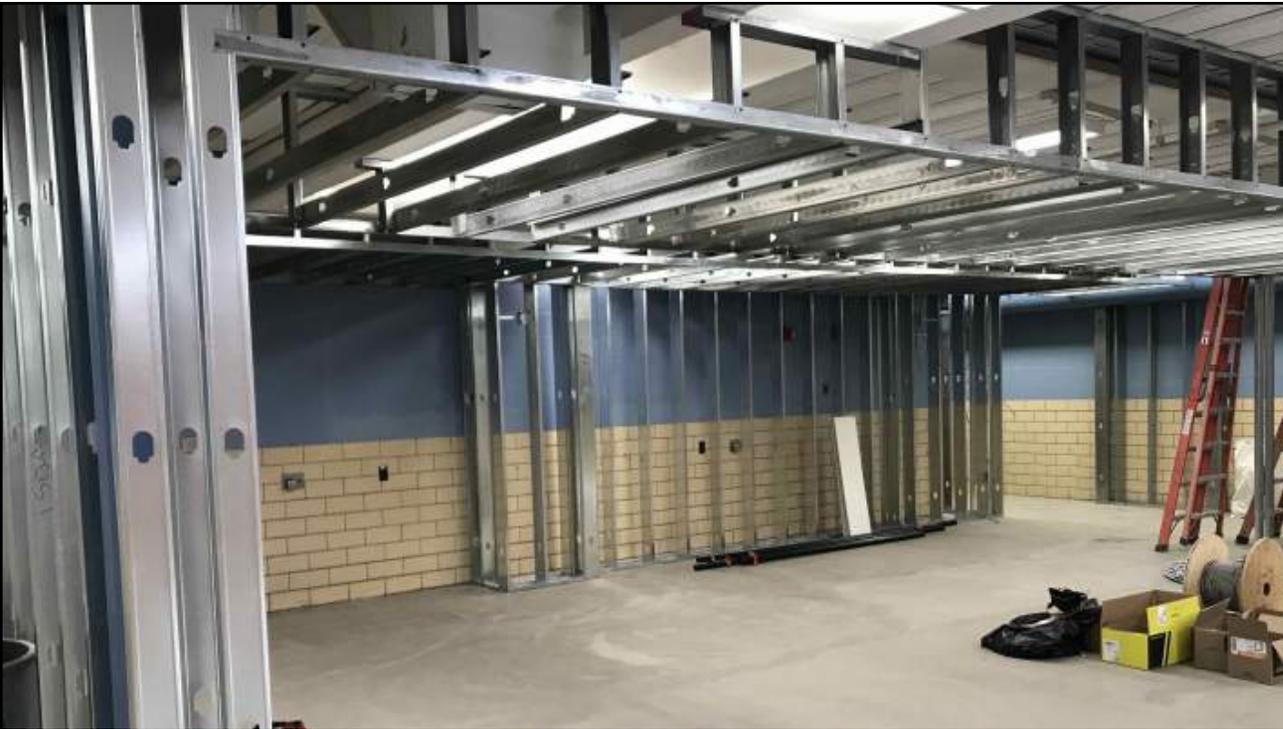

PHASE 3 PROGRESS PHOTOS



PHASE #4 CORRIDOR WORK HAS COMMENCED AHEAD OF ORIGINAL SCHEDULE.

PHASES 3 & 4 PROGRESS PHOTOS
