

HARVEY



NASHUA
SCHOOL DISTRICT
Gateway to Opportunity

NASHUA SCHOOL DISTRICT

JULY 2022 PROJECT UPDATES

- BRIAN S. McCARTHY MIDDLE SCHOOL
- PENNICHUCK MIDDLE SCHOOL
- FAIRGROUNDS MIDDLE SCHOOL
- 55 FRANKLIN ST.

BRIAN S. MCCARTHY

MIDDLE SCHOOL

CONSTRUCTION PROGRESS

■ SITWORK DEVELOPMENT -

- NEW ACCESS ROAD FROM BUCKMEADOW RD (DIANTONIO DR) - IN PROGRESS

- AUG. 2022 COMPLETION

- ELECTRICAL SERVICE TO BUILDING - SEPT. 2022

- TREE CLEARING/GRUBBING - COMPLETE

- UTILITIES/DRAINAGE - IN PROGRESS

- EMERGENCY ACCESS ROAD - ASPHALT (BINDER) - COMPLETE

- PARKING AREAS & ATHLETIC FIELD DEVELOPMENT - IN PROGRESS

- BLASTING - COMPLETE JULY 2022

■ BUILDING SEQUENCE = C → B → D → A

- AREA C -

- STEEL ERECTION - IN PROGRESS

- SLABS ON DECK - AUG. 2022 → SEPT. 2022

- ROOFING - LATE AUG. 2022

- AREA B - SLAB ON GRADE - COMPLETE

- AREA D - SLAB ON GRADE - COMPLETE

- AREA A - SLAB ON GRADE - AUG. 2022 → SEPT. 2022








PENNICHUCK MIDDLE SCHOOL CONSTRUCTION PROGRESS

- NORTH CLASSROOM ADDITION: COMPLETE = AUG. 2022
 - FINAL INSPECTIONS / CERTIFICATE OF OCCUPANCY = WEEK OF AUG. 22, 2022
- LEARNING COMMONS ADDITION: SCHEDULED COMPLETION = DEC. 2022
 - STEEL ERECTION – COMPLETE
 - EXTERIOR FRAMING & SHEATHING – IN PROGRESS
 - ROOFING – LATE AUG. 2022
 - MEPFP OVERHEAD ROUGH-IN – IN PROGRESS
- EXISTING SCHOOL (INTERIOR) RENOVATIONS:
 - SCIENCE CLASSROOMS/CAFETERIA/FOLDING PARTITIONS/CORRIDORS = FALL 2022 COMPLETION
 - GYMNASIUM = FALL 2022 COMPLETION
 - CURRENT MEDIA CENTER/LIBRARY RENOVATION = MID-SEPT. COMPLETION
 - TEMP. LIBRARY LOCATED IN NEW NORTH ADDITION UNTIL COMPLETION OF LEARNING COMMON ADDITION
- EXTERIOR BUILDING IMPROVEMENTS: SUMMER 2022
 - EXISTING ROOF REPLACEMENT, PERIMETER EDGE METAL, REMAINING MECHANICAL UNITS – FALL 2022
- SITE IMPROVEMENTS: COMPLETE AUG. 2022
 - CURBING, PAVING/STRIPING, SITE FURNISHINGS – COMPLETE
 - BUS LOOP FINAL PAVING – OCT. 2022
 - SCHOOL ENTRANCE & TRAFFIC CONTROL - COMPLETE
 - LANDSCAPING/IRRIGATION - FALL 2022

CONSTRUCTION PHASING & LOGISTICS PLAN (2022) REMAINING WORK PLAN - AUGUST 2022 UPDATE

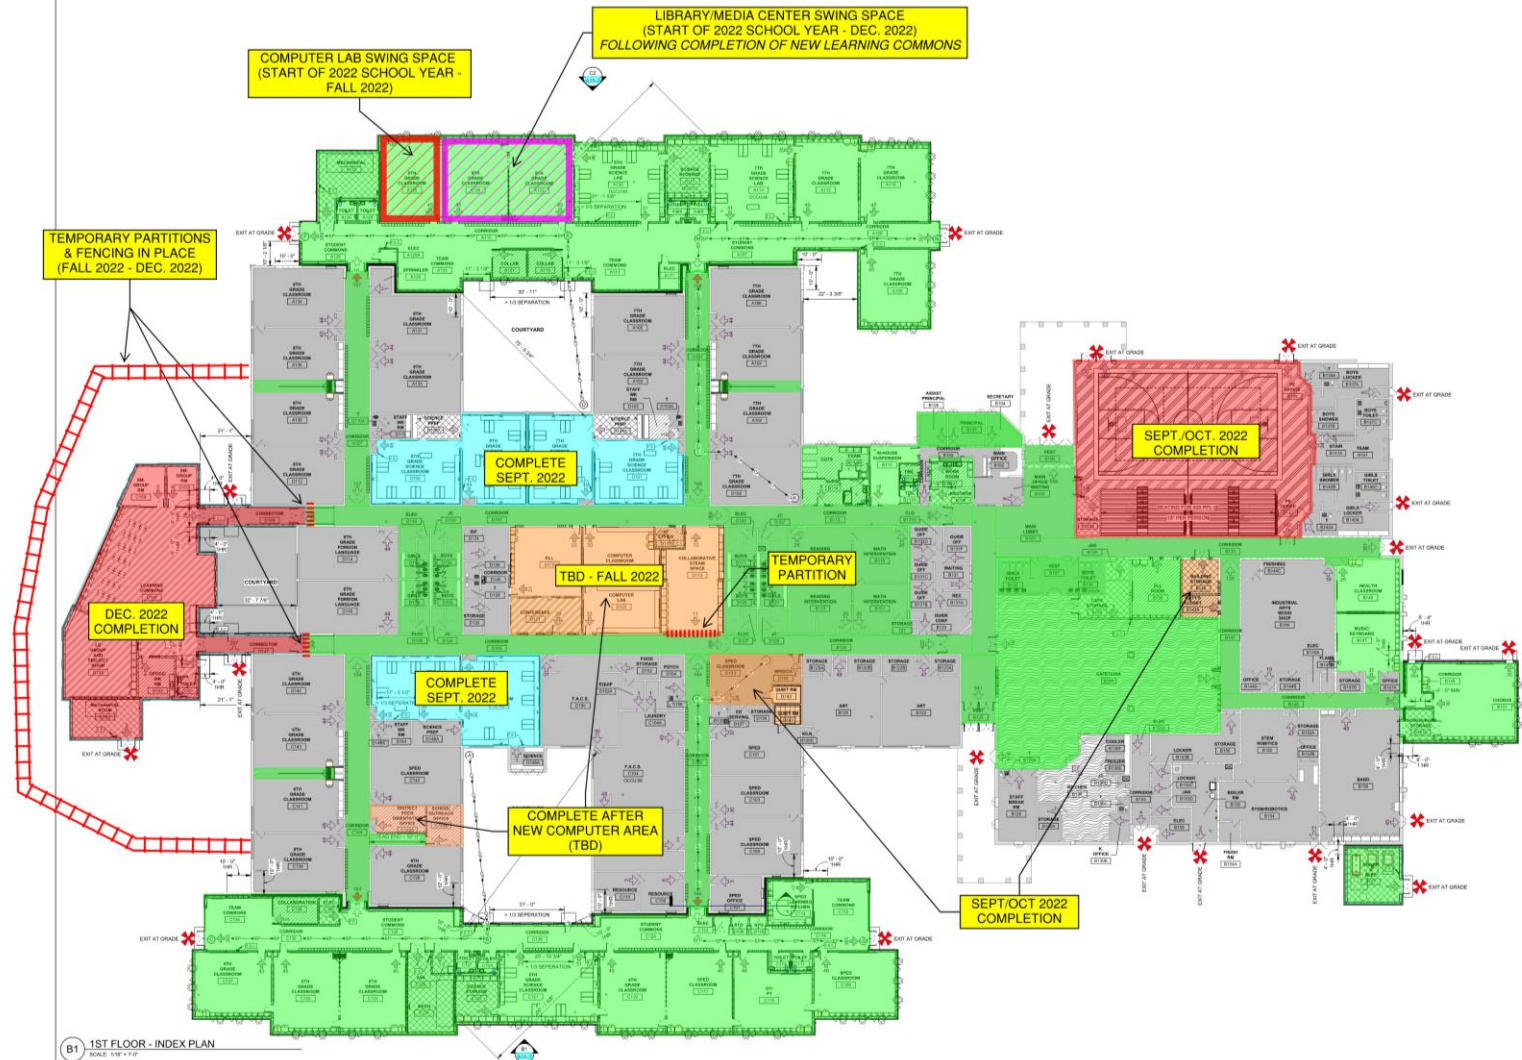











FAIRGROUNDS MIDDLE SCHOOL SUMMER 2022 RENOVATIONS



- LIBRARY/MEDIA CENTER – COMPLETE
 - PAINT CEILING/DUCTWORK/WALLS
 - CARPET/WALL BASE REPLACEMENT
- GUIDANCE/NURSE AREAS – COMPLETE
 - PAINTING/FLOOR & WALL BASE REPLACEMENT
- NEW SCIENCE ROOM D102 LAB TABLES – DELIVERED JULY 2022
- SCIENCE ROOMS D112, B113, B112 – AUGUST 2022 COMPLETION
 - NEW CEILING-MOUNTED CORD REELS
- EXTERIOR DOOR REPLACEMENTS (INCL. ABATEMENT) – COMPLETE
- WALL PROTECTION (ALL STUDENT COMMONS) – AUGUST/SEPTEMBER 2022 COMPLETION
 - WORK TO BE PERFORMED OFF-SHIFT IF CUSTOM FRP MATERIAL ARRIVES AFTER STUDENTS RETURN





55 FRANKLIN STREET EXTERIOR UPGRADES

- STRUCTURAL PREPARATION FOR EXTERIOR STAIRS - COMPLETE
- ADA RAMP - IN PROGRESS
- NEW 3RD FLOOR DOOR MASONRY WORK COMMENCING

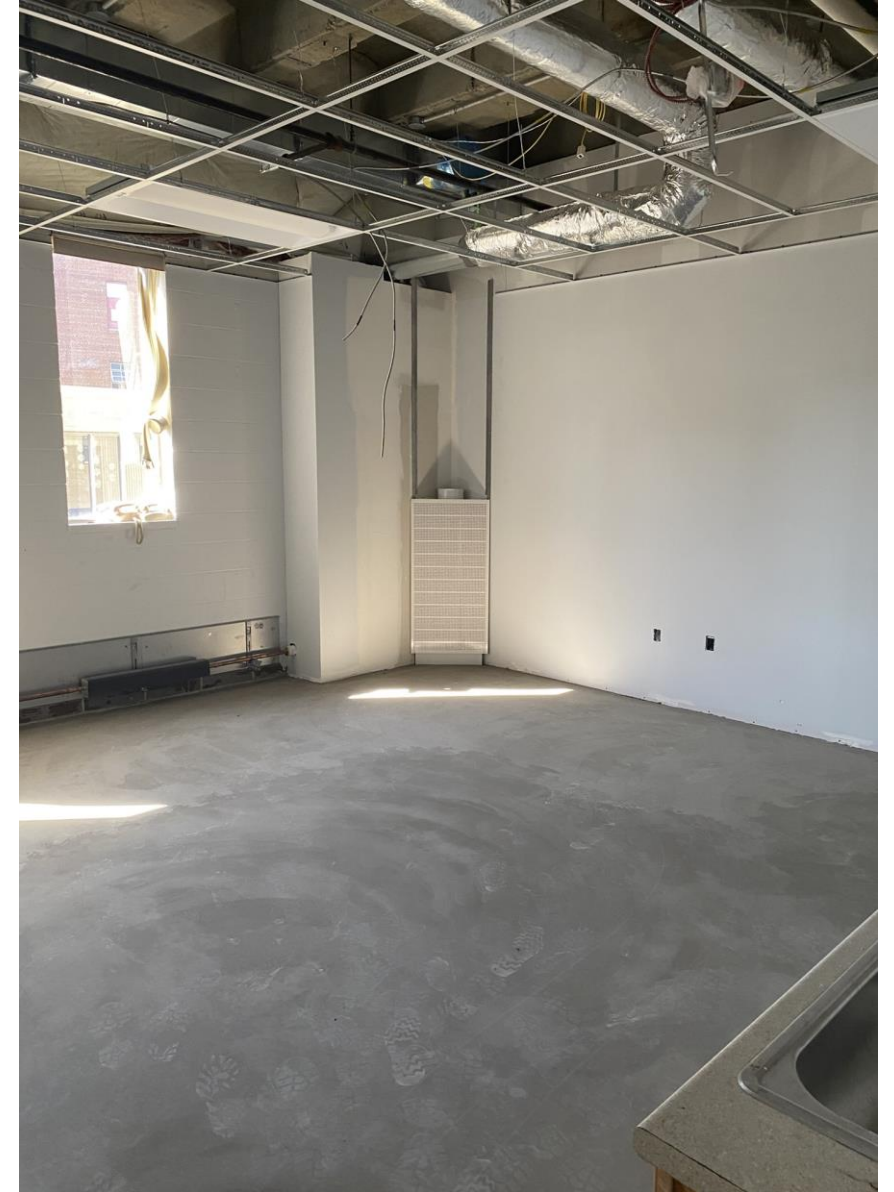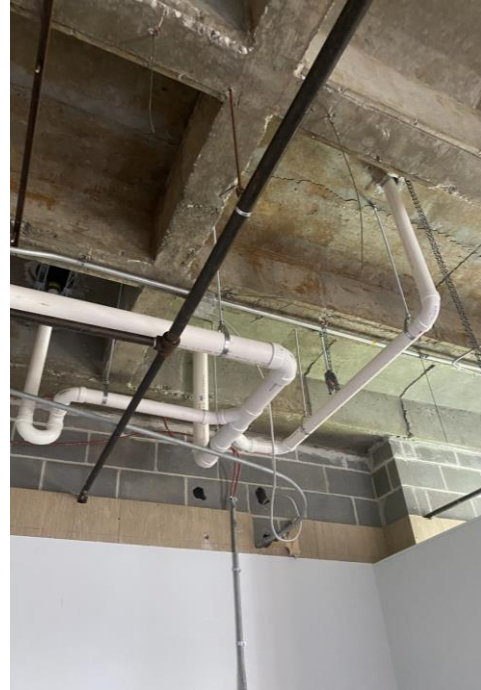

55 FRANKLIN STREET 2ND FLOOR CONSTRUCTION PROGRESS

- PAINTING AND FLOORING - ON-GOING
- RELOCATION OF FIRE ALARM DEVICES - IN PROGRESS
- DOOR INSTALLATION - ON-GOING
- INSTALLATION OF BATHROOM FIXTURES AND PARTITIONS - FALL 2022



HARVEY
