FAIRGROUNDS & PENNICHUCK MIDDLE SCHOOL ADDITIONS & RENOVATIONS NASHUA, NEW HAMPSHIRE

MARCH 2021 PROJECT UPDATES HARVEY CONSTRUCTION




PENNICHUCK MIDDLE SCHOOL CONSTRUCTION PROGRESS MILESTONES



FINALIZE GMP & TRADE CONTRACTOR AWARDS (MARCH 2021)


CONSTRUCTION START – NORTHEAST PARKING LOT (MARCH 2021)

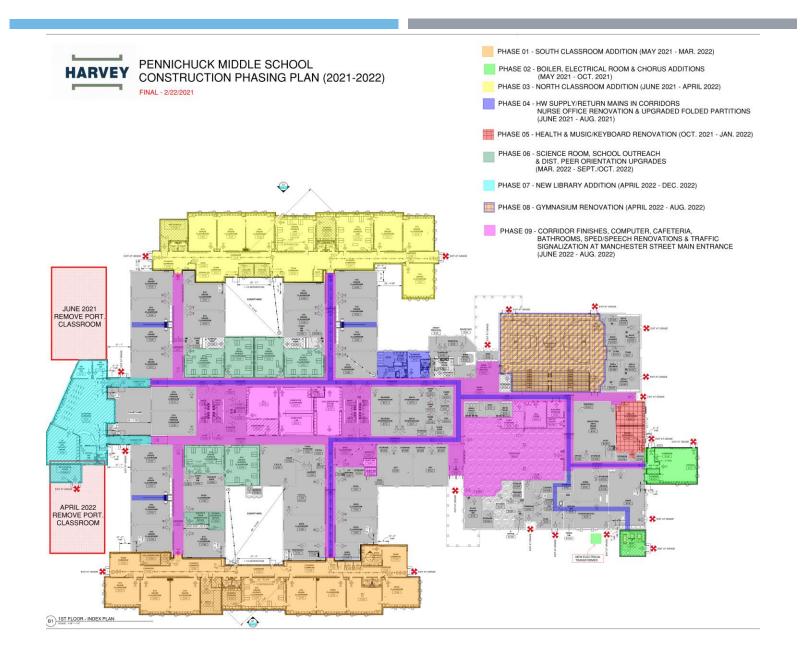

FAIRGROUNDS MIDDLE SCHOOL CONSTRUCTION MILESTONES:

- THE UNIFIED ARTS WING WAS SUBSTANTIALLY COMPLETED AND TURNED OVER ON 3/1/2021
- ADDRESSING HARRIMAN/HCC PUNCHLIST ITEMS WITH TRADE CONTRACTORS IN THE FIELD
 - ALL WORK PERFORMED IN OCCUPIED SPACES IS BEING COORDINATED IN CONJUNCTION WITH THE HYBRID LEARNING SCHEDULE
- SCIENCE ROOMS, CENTER "OCTAGON" AREA, & NEW ADMIN. AREA/ENTRANCE (APRIL 2021 COMPLETION)
- REMAINING SCIENCE ROOMS, GYMNASIUM, & EXTERIOR SITE FURNISHING/CLEANUP (APRIL 2021/JULY 2021)



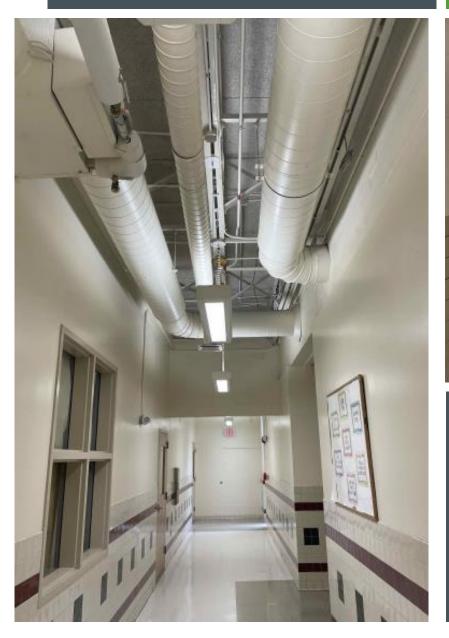






UNIFIED ARTS WING RENOVATIONS




CTE WORKSHOP RENOVATIONS



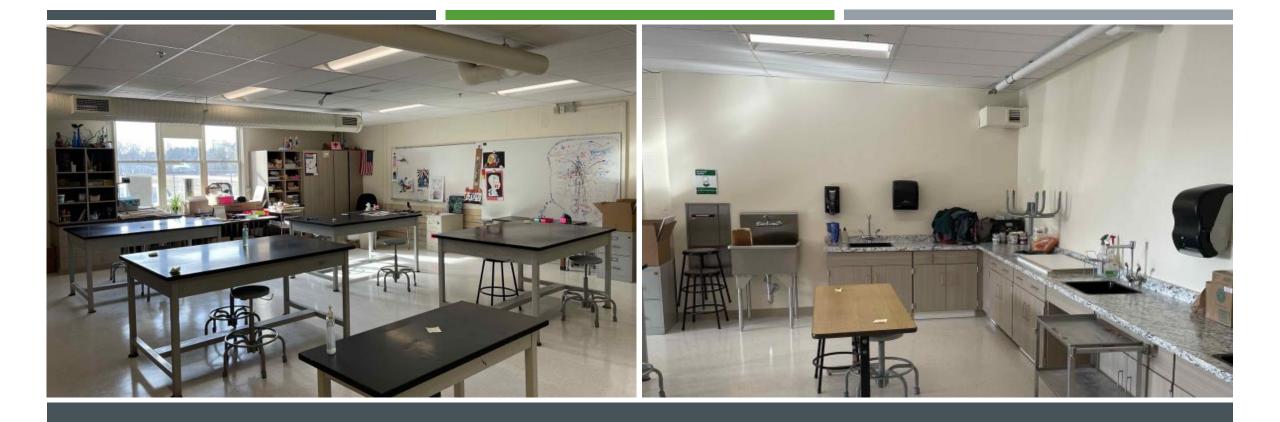

ART ROOM RENOVATIONS

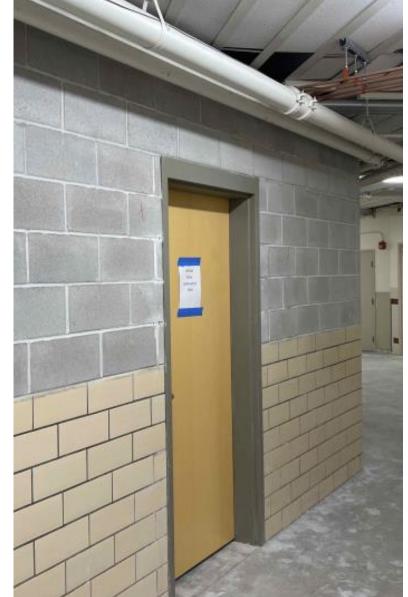





"OCTAGON" MAIN CORRIDOR CONSTRUCTION PROGRESS




NEW FRONT ENTRANCE CONSTRUCTION PROGRESS







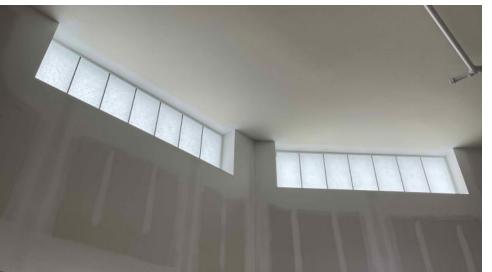

S.T.E.A.M. CLASSROOM CONSTRUCTION PROGRESS

